PRESENTATION FOR PROJECTS ,

AAY KAY ELECTRICALS PVT.LTD., – CAPABILITY PRESENTATION

WELCOME

AAYKAY ELECTRICALS PRIVATE LIMITED

An ISO 9001: 2008, D&B Certified Co

KEY INDEX:

1	COMPANY BRIEF
2	PROJECT PLAN
3	PROJECT CONSTRUCTION PROGRAM
4	PROGRAM METHODOLOGY FOR SITE LOGISTICS
5	QUALITY PLAN
6	MACHINERY TOOLS & INNOVATIVE IDEAS
7	INHOUSE & OUT SOURCED LABOURS IN ORGANIZATION
8	IMPROVING EXECUTION TIMELINE
9	CHECK LIST
10	PROJECT SAFETY PLAN FOR THE PROJECT
11	KEY ISSUES & RISKS
12	REFERENCE CHECK

COMPANY BRIEF

- AAYKAY ELECTRICALS PRIVATE LIMITED is one of the leading ISO 9001:2015,
  ISO 45001:2018 certified MEP contracting firm established in the year 2008.
- With its focus to deliver quality, safety, excellent service, customer centric approach, timely completion of projects and exceptional technical expertise in design, supply, erection, maintenance, testing & commissioning; AAYKAY has become one of the most preferred MEP contractor with top MNC's and Indian Client partners in short period of time since its inception in 2008.
- The company enjoys significant share of the domestic MEP market. This division of the company plays a pivotal role in the project execution of other service divisions organizations operations.
- AayKay has successfully completed projects in a wide range of market segments such as Banks, Hospitals, Industries, data centers, IT parks, Interior fit-outs, Substations, Commercial & High Residential Buildings.
- We have a highly skilled and dedicated site execution team of Project managers, Project Engineers, Safety and quality Engineers, Planning and Co-ordination engineers, Supervisors, Electricians and Offsite work force of Tender and Marketing Engineers, Procurement Engineers, Design Engineers, Billing Engineers, Accounts, Finance, HR and Administration team.

OUR WORK

We offer all-round electrical services solution

Our services cover internal & external electrical work as well as MEP

We assist with inspections of electrical systems & maintenance of electrical installations

We consult with project management consultants, architects, quantity surveyors, design consultants & real estate services companies


LEADERSHIP

- *I, Abdul Kareem P (B.Tech) have Vast experience of 30years in this filed like Base build, IT Workspaces, Labs, Data Centers, Hospitals, Industries, Commercial and High-Rise buildings.*
- *Over 16years, AayKay Electricals Private Limited has been committed to create well executed works in MEP business. We have clients who are confident on us continuously use our services for years. Most of them became our regular clients with our highly executed & satisfied works.*
- *Overcoming challenge after challenge with the support of my brilliant team, I have been successful in bringing Aaykay to a new milestone of Indian recognition.*
- *The journey of AayKay is never ending. But with the support of my team and clients, I am confident that the company will continue to scale milestones of excellence for years to come.*

Abdul Kareem P
Managing Director,
AayKay Electricals Private Limited.




COMPANY ESTABLISHMENT:

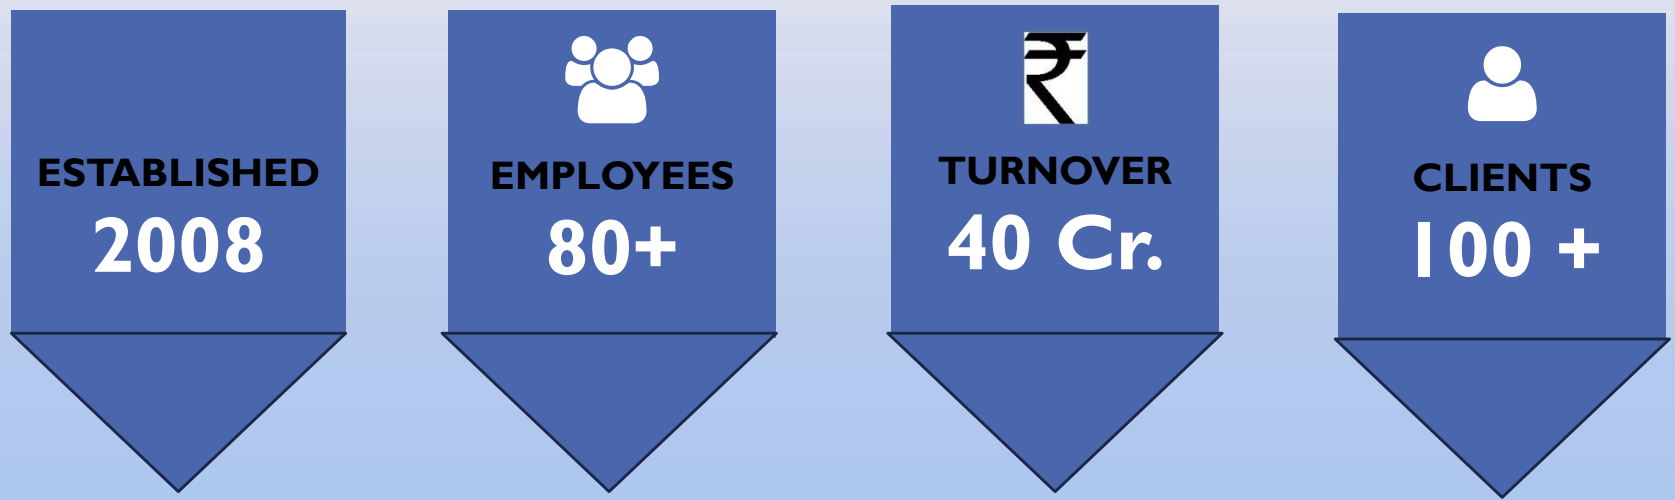

FINANCIAL YEAR	TURNOVER (INR)
FINANCIAL YEAR 2025-2026	RS. 40.11 CR.
FINANCIAL YEAR 2024-2025	RS. 37.32 CR.
FINANCIAL YEAR 2023-2024	RS. 35.44 CR.
FINANCIAL YEAR 2022-2023	RS. 36.87 CR.

COMPLIANCES & STATUTORY DOCUMENTS



GOVERNMENT OF INDIA
MINISTRY OF CORPORATE AFFAIRS

Central Registration Centre

Certificate of Incorporation

[Pursuant to sub-section (2) of section 7 and sub-section (1) of section 6 of the Companies Act, 2013 (18 of 2013) and rule 18 of the Companies (Incorporation) Rules, 2014]

I hereby certify that AAYKAY ELECTRICALS PRIVATE LIMITED is incorporated on this FOURTEENTH day of JANUARY TWO THOUSAND TWENTY FIVE under the Companies Act, 2013 (18 of 2013) and that the company is Company limited by shares

The Corporate Identity Number of the company is **U51100TS2025PTC192860**

The Permanent Account Number (PAN) of the company is **ABBCA9586A**

The Tax Deduction and Collection Account Number (TAN) of the company is **HYDA36506B**

Given under my hand at Manesar this FOURTEENTH day of JANUARY TWO THOUSAND TWENTY FIVE

Signature Not Verified
Digitally signed by DS MINISTRY OF CORPORATE AFFAIRS CRC MANESAR 1
Date: 2025.01.14 12:16:45 IST

Charan Singh
Assistant Registrar of Companies/ Deputy Registrar of Companies/ Registrar of Companies
For and on behalf of the Jurisdictional Registrar of Companies
Registrar of Companies
Central Registration Centre

Disclaimer: This certificate only evidences incorporation of the company on the basis of documents and declarations of the applicant(s). This certificate is neither a license nor permission to conduct business or solicit deposits or funds from public. Permission of sector regulator is necessary wherever required. Registration status and other details of the company can be verified on mca.gov.in.


Mailing Address as per record available in Registrar of Companies office:

AAYKAY ELECTRICALS PRIVATE LIMITED

HNO 6-3-652/D/13, FNO 1C, 1 FLOOR, DHRUVATARA APT, Somajiguda, Nampally, Hyderabad- 500082, Telangana

*as issued by Income tax Department

Certificate of Incorporation



CPG Certification Partner Global
ISO 45001 : 2018

CERTIFICATE OF REGISTRATION

THIS IS TO CERTIFY THAT THE OCCUPATIONAL HEALTH & SAFETY MANAGEMENT SYSTEM OF

AAYKAY ELECTRICALS PRIVATE LIMITED

**1st Floor, 6-3-652/D/13, Flat No 1C,
Dhruvatara Apartments, Panjagutta Road,
Behind Bank of Baroda, Somajiguda
Hyderabad-500082
Telangana INDIA**

has been assessed and registered as complying with the requirements of the International Standard shown above for the following Goods and Services. Further clarifications regarding the scope of this certificate and the applicability of the requirements of
ISO 45001 : 2018
may be obtained by consulting the certificate issuer.

IAF

Execution of HT & LT Electrification Works in Govt. Projects, IT, Non-IT, Industries, Residential Projects & Turn Key Projects.

JAS-ANZ
www.jas-anz.org/register

Tony Wilde
Group Chairman

Registration Number: OHS/6/SIN/22281
Current Registration Date: 09/Sep/2023
Expiry Date: 09/Sep/2028

Certification Partner Global
An Australian Owned Company
License # 1190/2011 CC (previously known as ISC Global),
Level 14, Boulevard Plaza, Tower 1, Downtown Dubai, Dubai, UAE

The Status and Validity of this Certificate maybe verified in real time by scanning the adjacent QR Code.

This certificate is valid until the Expiry Date shown on the condition that audits are conducted each year and paid for as per the Certification Agreement. Should this condition not be met, cancellation procedures will be initiated, and the cancellation status will be revealed when the QR Code is scanned.

This Certificate remains the property of CPG and must be returned upon request. It must not be altered in any way. Intentional misuse of this certificate will result in cancellation without prior notification

OHSMS 45001: 2018



CPG Certification Partner Global
ISO 9001:2015

CERTIFICATE OF REGISTRATION

THIS IS TO CERTIFY THAT THE QUALITY MANAGEMENT SYSTEM OF

AAYKAY ELECTRICALS PRIVATE LIMITED

**1st Floor, 6-3-652/D/13, Flat No 1C,
Dhruvatara Apartments, Panjagutta Road,
Behind Bank of Baroda, Somajiguda
Hyderabad-500082
Telangana INDIA**

has been assessed and registered as complying with the requirements of the International Standard shown above for the following Goods and Services. Further clarifications regarding the scope of this certificate and the applicability of the requirements of
ISO 9001:2015
may be obtained by consulting the certificate issuer.

IAF

Execution of HT & LT Electrification Works in Govt. Projects, IT, Non-IT, Industries, Residential Projects & Turn Key Projects.

JAS-ANZ
www.jas-anz.org/register

Tony Wilde
Group Chairman

Registration Number: QMS/15/SIN/2281
Current Registration Date: 09/Sep/2023
Expiry Date: 09/Sep/2028

Certification Partner Global
An Australian Owned Company
License # 1190/2011 CC (previously known as ISC Global),
Level 14, Boulevard Plaza, Tower 1, Downtown Dubai, Dubai, UAE

The Status and Validity of this Certificate maybe verified in real time by scanning the adjacent QR Code.


This certificate is valid until the Expiry Date shown on the condition that audits are conducted each year and paid for as per the Certification Agreement. Should this condition not be met, cancellation procedures will be initiated, and the cancellation status will be revealed when the QR Code is scanned.

This Certificate remains the property of CPG and must be returned upon request. It must not be altered in any way. Intentional misuse of this certificate will result in cancellation without prior notification

ISO 9001-2015



Electrical License(HYD).




ಕರ್ನಾಟಕ ರಾಜ್ಯ KARNATAKA STATE
CLASS I ELECTRICAL CONTRACTOR LICENSE
ವಿದ್ಯುತ್ ಪರಿವೀಕ್ಷಣಾಲಯ
DEPARTMENT OF ELECTRICAL INSPECTORATE

Electrical License(BLR).



Employee State Insurance




Employee Provident Fund




UDYAM REGISTRATION CERTIFICATE

MSME Certificate



Government of India
Form GST REG-06
(See Rule 10(1))
Registration Certificate

GST Registration Certificate



आयकर विभाग INCOME TAX DEPARTMENT
भारत सरकार GOVT. OF INDIA
e - Permanent Account Number (e-PAN) Card

PAN Card

OUR BRANCHES



- TELANGANA (HYD) (HQ)
- ANDHRA PRADESH
- KARNATAKA
- MAHARASTRA
- TAMILNADU
- WEST BENGAL
- HARYANA

PROJECT Criteria

1. Technical Criteria

Technical Specifications
Quality Standards
Compliance Requirements
Tools & Technologies

2. Financial Criteria

Budget Allocation
Cost Control Measures
Payment Schedule
ROI Expectations

3. Timeline Criteria

Project Schedule
Task Breakdown
Deadlines
Contingency

4. Resource Criteria

Human Resources
Material Requirements
Equipment & Machinery
Vendor Requirements

5. Risk Assessment Criteria

Identified Risks
Mitigation Strategies
Safety Protocols
Contingency Planning

6. Quality Assurance Criteria

Inspection Process
Testing & Validation
Documentation Requirements
Approval Procedures


7. Communication Criteria

Reporting Format
Meeting Schedule
Communication Channels
Escalation Matrix

8. Conclusion

Summary of Key Criteria
Approval Needed
Next Steps

DESIGN METHODOLOGY :

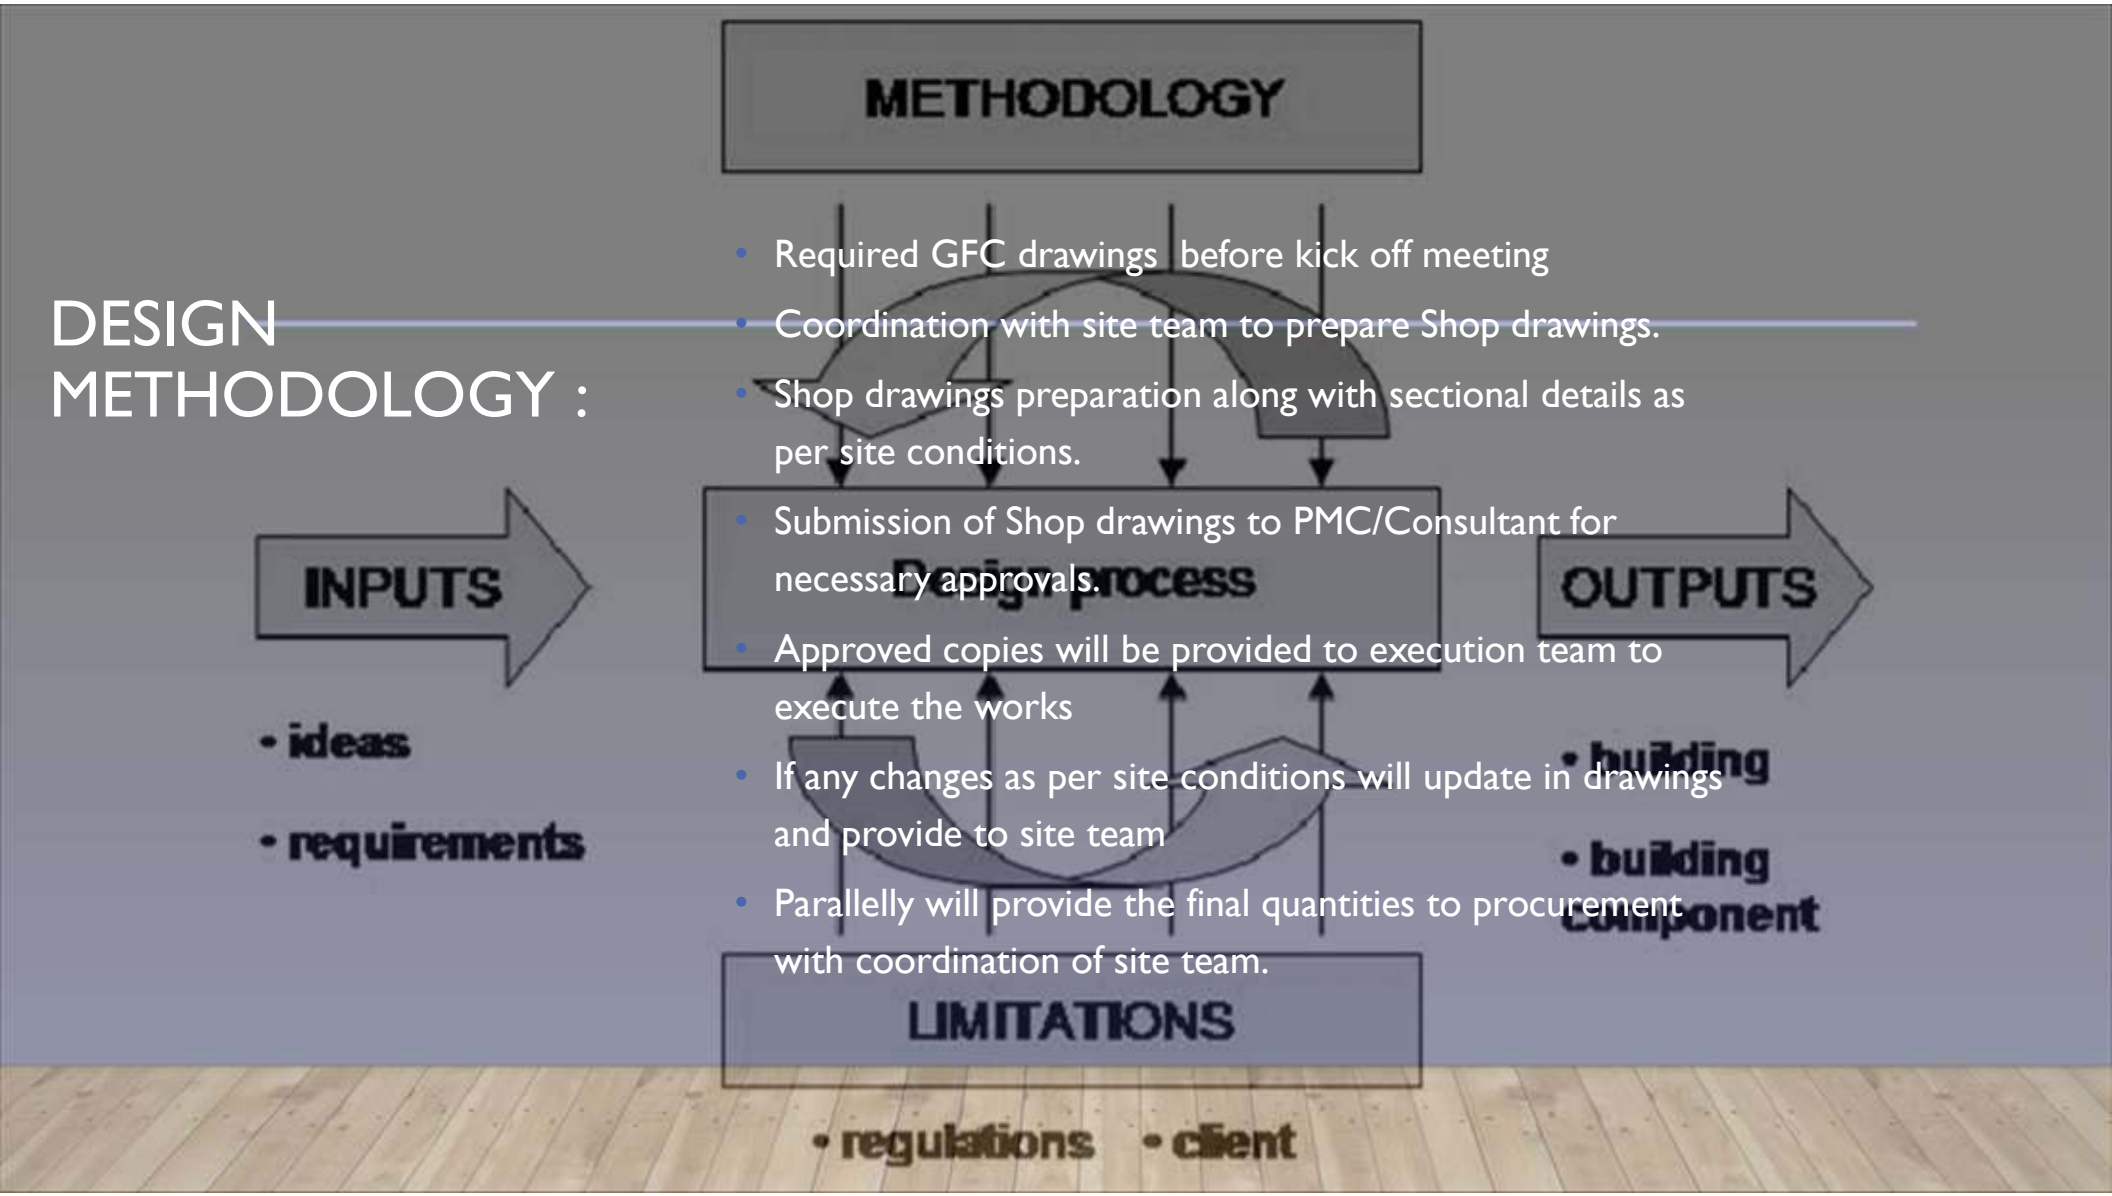

- Required GFC drawings before kick off meeting
- Coordination with site team to prepare Shop drawings.
- Shop drawings preparation along with sectional details as per site conditions.
- Submission of Shop drawings to PMC/Consultant for necessary approvals.
- Approved copies will be provided to execution team to execute the works
- If any changes as per site conditions will update in drawings and provide to site team
- Parallelly will provide the final quantities to procurement with coordination of site team.

PROJECT METHODLOGY

To have the perfection in the work, we follow the work execution check list at site during execution of work. This ensures that all the works are completed within the specified time and there is no compromise in the quality.

Our Site Team regularly updates the lists with the developments at the site so as to avoid any gap / discrepancies .

Following are the check lists for various works :

- Checklist of Conduiting & Wiring
- Checklist of Cable Trays & Raceways
- Checklist of Under Floor Trunking
- Checklist of Cables and Fixtures
- Checklist of proper Earthing
- Checklist of Panels & DB's

:

PROJECT STAGE WISE STRATEGY & TECHNIQUES:

I Design

- GFC Drawing
- Review
- Shop Drawing
- GA Drawing
- Technical Submittals

II Procurement

- Vendor Validation
- Supply Chain Management
- Procurement Process
- ERP
- Tracking Material

III Construction

- Secure The Location
- Material Stacking
- Flow Chart
- Risk Analysis
- Safety

IV Testing & Commissioning

- Work Evaluation
- Functional Verification
- Visual Verification
- GA Drawing
- Quality/Safety Checks

V Handing Over

- Test Report
- Warranties
- Training
- Sign Off



METHOD STATEMENTS

CASE STUDY & MITIGATION PLAN

1. Required GFC drawings before kick off meeting
2. Samples & TDS approval with in 5 days
3. Panel GA Drawings & Shop Drawings approval with in one week
4. Required Reflected Ceiling Plan layouts
5. IT vendor power / raceway requirements
6. Workstation Leg marking for marking of floor raceways
7. HVAC power requirements

Electrical Works – Project Schedule

1. Mobilization & Preparation

Site handover & inspection Safety induction & manpower deployment Material procurement plan and vendor finalization Storage area setup for electrical materials Coordination meeting with client/PMC/civil team.

2. Conduiting & Cable Tray Works

2.1 Conduiting Marking & layout Conduit laying in slabs, walls, and floors Sleeve provisions Back-box installation.

2.2 Cable Tray Installation Horizontal & vertical cable tray fixing GI supports fabrication & installation Trunking work

3. Wiring & Cabling Works

3.1 Power & Lighting Wiring Light point wiring Power point wiring DB to equipment wiring Earthing wire routing.

3.2 HT/LT Cabling Cable route marking Cable laying Cable dressing & tagging Glanding & termination

4. Electrical Panels & DB Installation

MDB/SMDB installation DB installation & wiring Control wiring Panel earthing Panel testing---

5. Light Fixtures & Accessories Installation

LED lights installation Switches & sockets Exhaust fans, ceiling fans Junction box terminations---

6. Equipment Installation

UPS installation AC units electrical connection Server room electrical works Pumps/Motors electrical hookup---

7. Earthing & Lightning Protection

Earth pits construction Earthing grid & GI strip laying SPD installation Lightning arrestor installation---

8. Testing & Commissioning

Megger testing IR test, continuity test Panel load test Light testing & circuit verification HT/LT equipment testing---

9. Final Checks & Handover

As-built drawings Test reports submission Snag rectification Final walkthrough with client Project handover

SAFE METHOD OF STATEMENT

ELECTRICAL WORKS

Working Procedure For Electrical Installation Works

SAFE METHOD OF STATEMENT

ELECTRICAL WORKS

II. CONTENTS

SL. No	Description	Pages
1	Scope	3
2	Purpose	3
3	Applicability	3
4	Reference Documents	3
5	Responsibilities	4
6	Prerequisite	5
7	Precautions	5
8	Equipment /instruments/Accessories	6
9	Installation of cable tray	6
10	Acceptance Criteria	10
11	Attachments	10
12	Distribution	10

SAFE METHOD OF STATEMENT

ELECTRICAL WORKS

Scope:

This Working Procedure describes the Method of unloading, Storage and fixing the following works
Conduiting Wiring for lighting & Power Points
Installation of wiring accessories
DB
Light Fixtures
Earthing
Cable Tray and Support
Cable Laying, Glanding & Termination
LV Panel
UPS/Inverter

SAFE METHOD OF STATEMENT

ELECTRICAL WORKS

Purpose:

Purpose of this Working Procedure is to provide necessary documentation to carry out Inspection, Storage and fixing in a systematic way and maintain proper records.

Reference Documents:

Technical Specification
Relevant approved Material Submittal, Technical Data Sheet
Approved Shop Drawings
Relevant Codes/Standards

Responsibilities:

The responsibility of ensuring the implementation of this Working Procedure rest with Project Manager.

SAFE METHOD OF STATEMENT

ELECTRICAL WORKS

Site In charge

Site In charge will be responsible but not limited to the Following activities:
Identify and reporting to Project Manager for any non-conformance.
Control point clearance with contractor.
To ensure that the relevant Project Specification, Approved Working Procedure and Approved shop drawings are available at site.
To check the access and area for installation.
To ensure safe unloading / shifting at site.
To ensure that the installation is done at site as per approved shop drawings.

Pre-requisite:

All workers engaged for unloading shifting and to attend safety induction conducted by safety officer and specific training by Site Engineer / Supervisor on the laying method to be adopted at site.
Availability of material handling equipment of adequate capacity required to carry out the works.
Inspection of site area and access prior to commencement of works.
Availability of all relevant documents i.e. approved drawings, material submittal, Data sheet, Method Statement and Factory Test Report to be checked by the Site incharge.

SAFE METHOD OF STATEMENT

ELECTRICAL WORKS

Precautions

All work men shall be given safety pep Talk once a month and the same shall be recorded.
Work will commence as per safety regulations laid down in the contract specifications and project health , safety and environment plan
Proper safety harness must be used.
All personal protective equipment (PPE) has to be used.
Housekeeping shall be as per standard and all debris to be removed from work place after completion of work every day.

SAFE METHOD OF STATEMENT

ELECTRICAL WORKS

- **Acceptance Criteria**
- Technical Specification
- Approved shop Drawing
- Project safety plan
- **Distribution**
- Project Manager
- Site in charge
- Contractor

Installation Method Conduiting; Fixing of conduit .

Selection of conduit diameter will be as per approved drawing.
Conduit routing shall be marked on wall/ceiling according to site condition and approved working drawings.
Selected conduit shall be cut with hacksaw to the correct sizes, file the conduit to remove burrs.
Threading will be done by threading machine .minimum 6 thread shall be attended properly.
Selection of Conduit support system as per approved Drawing and site condition.
Hole shall be drilled on wall / ceiling as per site condition. Nylon/PVC Plug shall be inserted inside the drilled hole.

SAFE METHOD OF STATEMENT

ELECTRICAL WORKS

All conduits shall be run on spacer saddles and clamped at interval not exceeding 2.50m in horizontal & 1.50m vertical direction. Screw the conduit clamp with proper screw endering inside the Nylon/PVC plug.
Adequate size of GI wire (pulling wire) shall be provided .
Verticality and horizontality shall be maintained properly.
Installed conduits shall have their ends closed by caps or plugs, which shall remain in place untill wires are pulled.
Conduits will be cleaned out thoroughly before pulling cables in to them by using of blower.

Wiring for lighting & Power Points.

The wires & cables will be installed in conduits, trunking and ladders as per the approved shop drawings
For the light & Power circuits, wires & cables will be used as per the approved material submittal.
Before starting the wiring for the above mentioned activities, we have to make sure that the plasterwork is finished completely in that area / floor & there is no more water still on the walls.
Before start pulling the wires we will be sure that there is no water or any rubbish inside the conduits.

SAFE METHOD OF STATEMENT

ELECTRICAL WORKS

At the false ceiling area, we have to use a ceiling rose with a heat resistance wire & where are coming a gypsum board ceiling we have to extend the wires from the slab to the expected level of the gypsum ceiling through a flexible conduits.

Lighting & Power circuits will be run in separate conduits.

For branch circuit work, originating from light & power panel boards will be arranged as per the approved drawings. Loads on various phases of panel boards will be balanced as per he approved load schedules.

For avoiding any damaged for the conductors, insulation or jacket of the wire or cable during the pulling stage, and lubricants will be used properly to prevent any stresses on conductors. For pulling the wires, we will install 3mm galvanized standard steel wire with wooden blocks fastened at ends in empty service conduits.

At every branch circuit outlet & pull-box, every cable passing through will be left slack to allow inspection & for connection to be made. Cables terminating in outlet boxes will be left with at least 250mm extra length for terminations.

All circuits will be properly labelled during the pulling work to facilitate the terminations at the respective devices.

After the pulling circuit works completely, all the circuits will be checked & tested if any open circuits, short circuits, earthing continuity & excessive resistance or leakage.

SAFE METHOD OF STATEMENT

ELECTRICAL WORKS

Installation of wiring accessories

Check whether location for fixing Plug and socket is ready as per approved drawing.
Plug and Socket will be handled carefully as they are fragile item.
Installation shall be done as per manufacturer manual.
After installation of Plug box gaps should not be their visible.
Tight fixing rigidity shall be ensured.
Verticality/horizontality shall be ensured with the use of spirit level.
Housekeeping should be done everyday.
Tightness of Screws shall be ensured with Screw driver set. Extra knockout shall be closed to prevent from dust and foreign materials.
Sticker will be provided on every Plug box indicating their functionality.
The Switches shall be fixed to wall or column at level 1350mm above the finished floor level /as per approved drawings.
The Outlet shall be fixed to wall or column at level 300mm above the finished floor level / as per approved drawing.

SAFE METHOD OF STATEMENT

ELECTRICAL WORKS

Ø DB Installation

All Incoming/Outgoing feeders for individual panels shall be as approved GA diagram.

As per approved equipment layout arrange all the DB's as per location specified in the drawings.

For wall mounted DB's shall be fixed properly by using special anchor fastener for Brick wall/hollow wall.

DBs shall be fixed with bottom at 1800 mm from FFL and in accordance with the manufactures recommendation/as per approved drawings.

All exterior and interior steel surfaces of the Panel Boards will be properly cleaned after completion of work and all rubbish, dust or concrete spatter will be removed from inside and around the Panel Boards by using brushers, vacuum cleaner etc.,

Ø Installation of Light Fixture.

Light Fixture shall be installed as per approved shop drawings.

Wires brought out from junction boxes shall be encased in GI/PVC flexible pipes as required for connecting to the fixtures concealed and is suspended from ceilings. Flexible pipes shall be provided with check nuts at both ends.

All suspended fixture shall be mounted and fixed in position in accordance with drawings.

Fixture shall be suspended true to alignment, plumb, level and capable of resisting all lateral and vertical forces.

All suspended light fixture shall be provided with concealed suspended arrangement in the concrete slab/roof.

SAFE METHOD OF STATEMENT

ELECTRICAL WORKS

Wires shall be connected to all fixtures through connector blocks/cage clamped.
Flexible conduit should be of PVC.
All lighting fixtures, when installed shall be set true and free of light leaks, warps, dents and other irregularities. The finish of exposed metal parts of lighting fixtures and finish trims of all recessed lighting fixtures shall be as directed by the Employer or as indicated on the Drawings.
After the fixtures are completely installed, the wiring system, wiring and fixtures must be tested against grounds and short circuit.
Power for normal lighting shall be obtained from normal supply lighting panel
Power supply for emergency lighting shall be obtained from very- essential lighting panel which are fed directly by the UPS system.
Distribution of lighting power at one location shall be to all three lines and Neutral. **Earthing**
Earthing Strip (GI/Copper) size will be as per approved lay out drawing.
Earthing Strip (GI/Copper) will be free from laminations, rust, scale and other Electrical mechanical defect.
Strip will be made straight before installation.
Conductor to be cut by cutting machine or hand held hacksaw.
Drill a hole with a proper drilling machine for bolted joint.
All Earth conductor joint shall be welded as per approved drawing.

SAFE METHOD OF STATEMENT

ELECTRICAL WORKS

Pipe Earthing Station

The earth electrode shall be 2.5m long, 50mm diameter, 5mm thick galvanized steel pipe. The earth resistance shall be maintained with a suitable soil treatment as shown on approved working drawings and as per plate
Electrodes. The resistance of each earth station should not exceed 2 Ohm. In case of values exceeding 2 Ω the earth lead shall be fixed to the pipe with a clamp and safety set screws. The clamps shall be permanently accessible.

Plate Earthing Station

Excavation on earth for a normal earth Pit size is 600 mm X 600mm X 3000mm.
Use 19 mm GI Pipe/600X600X3.15 mm cu plate for more contact of earth and reduce earth resistance.
Make a mixture of Wood Coal Powder Salt & Sand all in equal part

Ø Installation of MS supports and cable Tray .

Pre-installation

The route survey for laying cable trays shall be done as per Approved Drawings. Any hindrance at site due to other system works shall be reported to Contractor
Availability of all Tools/Tackles/Manpower shall be verified with the concerned personnel related to the activities.
For accessibility necessary scaffolding arrangements shall be made.
Select the cable tray as per approved Layout drawing
Safety Precaution should be taken while installation of Cable tray like Hot work permit, Area barrication, safety check of ladders and scaffolding etc.

SAFE METHOD OF STATEMENT

ELECTRICAL WORKS

Installation of supports

Measure the Civil cut out provided as per approved drawings /Site condition.
As per approved drawings, arrange the entire Angle for Panel Cut outs required per location specified in the drawings.
Measure the Angle size delivered at site. The size of the angle should be 50X6 mm.
Cut the angle by hacksaw machine/Motor driven machine to suit the cut out size and as per site condition.
Place the L-angle at four corner of Cut out.

Installation of GI Cable Trays

Cable trays shall be cut with hacksaw to proper length as per site requirements.
Sharp cutting edges shall be filed using suitable file.
Hole shall be made for couplers, with drilling machine for suitable size to match the coupler plate and coupler joints shall be tightened with necessary nuts & bolts as per requirement. Coupler to be provided at both sides of the tray up to 300mm tray and for more than 300mm tray one extra coupler shall be provided at the bottom of the tray.
Level the support prior to installation of cable tray.
Allotment of cable tray for Power cable, control cable and SMS cable shall be as per approved drawings.
Any cut on cable tray should be painted with Zinc chromate paint.
Cable tray support should be comprise of min 10mm and 12mm anchor fastner,10mm and 12 mm threaded rod and rigid support should be provided at after 30 meter or two adjacent bend whichever occurs first
.Rigid support should of C-channel and Angle support .
Cable tray or ladder shall not be installed across building or structural expansion joints.

On horizontal runs the tray or ladder shall be installed with a 20 mm gap at the expansion joint. Supports shall be installed within 150 mm on either side of the joint.

Each section of the cable tray shall be electrically bonded with GI Strips as per approved shop dwg.

Laying of cables

Identify the right type of cable for its cross sectional area, type, no of cores ,Voltage grade etc before unwinding from drum .

Both ends of the cable shall be water sealed until termination.

Jack up the drum , unwind the cable and pull over to roller .

Meggering of cables should be done before unrolling from drum and after cutting record the reading.

The measurement of the Cable at different routes/equipment to be taken in advance to cut the cables from the right drum (drum schedule) to avoid cut lengths of cable in the drum

Cables shall be routed as per the cable schedule.

Sagging of the cable shall be avoided.

Power and control cables shall be laid in separate cable trays of adequate width , the support of cables to suit the span and weight of the cables as per approved Standard support details .

Care should be taken to avoid sharp bending of cables, damaging of insulation while pulling, laying and stripping the cable.

Where cables are buried in the ground the minimum depth of burial shall be 600mm. and covered by a 75mm layer of clean sand or indicated in Bureau of Indian standards . Cables marking tape and the trenches backfilled to grade level

All cable shall be identified by means of cable tags tied at the cable end visible properly.

Cable shall be laid in one continuous length.
Cable shall be laid with a spacing of 1d (preferred).
Cable shall be laid in the cable tray having 20% spare space .

Glanding &Termination

The suitable size/type of the cable gland to be used shall be identified with the size of the cable.
Termination shall be done as per the approved cable schedule.
Each wire shall have required extra length before termination point.
Earth wire shall be connected to the ground bus as per the Drawing.
Provide ferrule as per cable schedule
Sub-circuit wiring for lighting shall be carried out in looping system. Joints shall be made only at distribution board terminals, switches/buzzers and at ceiling connectors/lamp holders terminals for lights/fans/socket outlets. No joints shall be made inside conduits or junction/draw/inspection boxes.
Switches controlling lights, fans or socket outlets shall be connected in the phase wire of the final sub circuit only.
Switches shall never be connected in the neutral wire.
Conductors having nominal cross sectional area exceeding 1.5 sq. mm shall always be provided with crimping sockets.
Care shall be taken for uses of all three phases for distribution to lights of same area , and
Nickel coated nuts and bolts shall be used for all connections.
Glanding will be done by double compression brass gland.

SAFE METHOD OF STATEMENT

ELECTRICAL WORKS

LV Panels .

Crane/Hydra shall be used for unloading of panel.
The Panel accessories will be kept in secured location.
Panel shall be lowered at platform level with crane or Hydra. From there we sue manual methods using pipe roller, Sleepers and Craw bar for shifting and unloading of panel.
If location is not ready then Panels will be kept on Store yard on wooden planks , and it should be covered (preferable placed at covered place).
Panels stored at the yard will be shifted to the location using Crane, Hydra or trailer with proper support and care.

Check up the panel Location and ensure that the same is as per approved Lay out Drawing.
Place the level of panel on the frame provided at location.
Install the LT Panel, capacitor bank and its accessories as per approved Drawings
Where panel will come in different sections bus bar joints shall be tightened with torque Wrench to ensure Torque as per specification or manufacturer Manual.
Thoroughly clean the joint surfaces
Leave space of minimum 750mm at the back of the panel. Also provide rubber mat in front of the panel as per approved drawings
Openings / Gaps in the panel bottom shall be thoroughly sealed by rubber gourmet.
Connect double earthing with the panel where the provision is made.


SAFE METHOD OF STATEMENT

ELECTRICAL WORKS

UPS/INVERTER

All Incoming/Outgoing feeders for individual panels shall be as approved GA diagram.
Installation will be done as per Installation detail drawings of Cables & Raceways and its accessories connected with the UPS and Stationary Batteries.
As per approved equipment layout arrange all the UPS as per location specified in the drawings.
UPS/Inverter shall be installed as per manufacturer recommendation.
Proper body earthing connections to the UPS/Inverter has to be done.
Proper Neutral earthing connections to the UPS/Inverter has to be done.
All batteries terminals are to be tightened properly.
Check the polarity of all batteries connected in the bank

LOGISTIC CHART

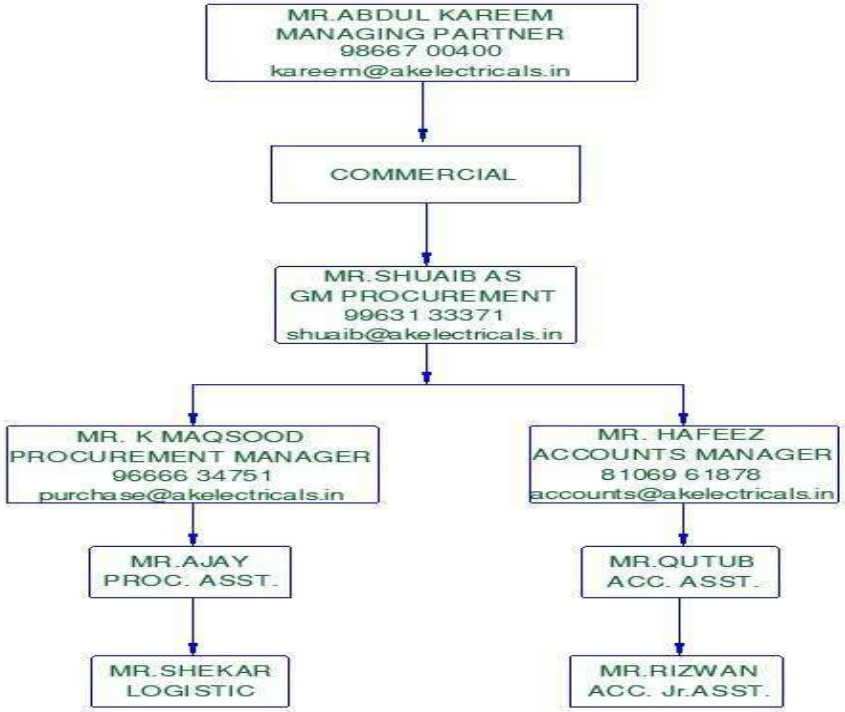

LOGISTIC PLAN

LABOUR MOVEMENT

- Entry and exit will be at one location
- Security check point to control labour entry/exit
- Entry will be by batches
- ID card for labour after induction
- Labour frisking for all labour entry
- Defined walkway for labour
- Emergency assembly point at ground floor

MATERIAL MOVEMENT

- Entry and exit will be at ground floor
- Material shifting will be done through service lift
- Safety team to check vehicle before allowed into site premises
- Designated place for unloading and likewise for loading
- Separate place for debris yard & scrap yard
- Separate place for waste management

GENERAL PROVISIONS

- Designated space for first aid room as per standard requirement
- Designated space for induction room
- Separate place for site office
- Drinking water point
- Placing of adequate fire extinguisher
- Emergency exit signage

QUALITY PLAN:

- Responsibility of Policy Issues. Establish QA Requirements through client liaison. Notify Project Manager of necessary documentation.

- Ensures QA Procedures carried out & correlates documentation with Project Manager. Checks documentation & receives feedback on QA system effectiveness. Receives & documents client Feedback.

- Quality Control Supervisor: Files and actions documentation. Liases with client QA inspectors. Reports Non-Conformities. Ensures work carried out to program, Assists Project Manager, Carries out QA Checks and fills out documentation.

HIGH QUALITY EXECUTION










QUALITY EXECUTION

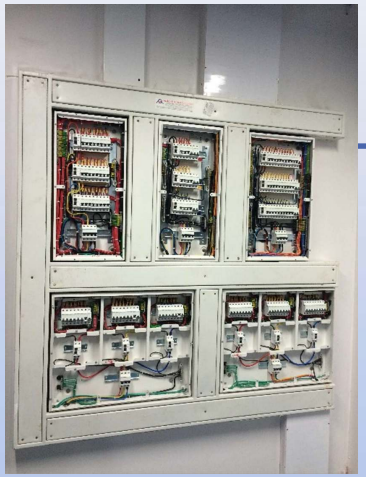












CLIENT APPRECIATIONS:

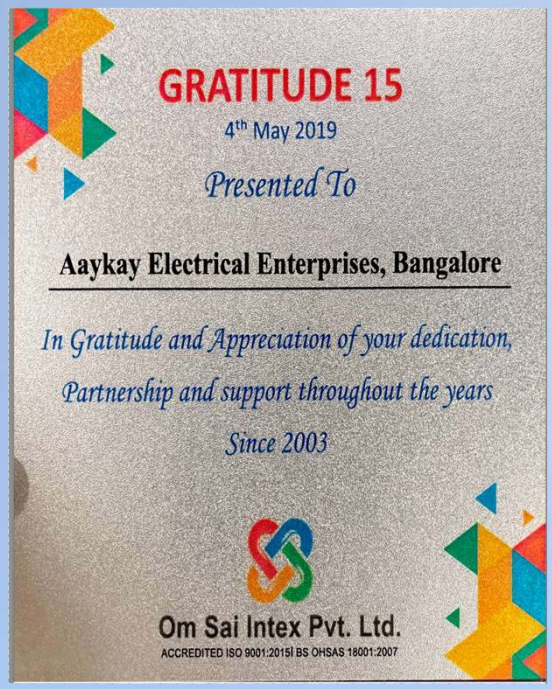

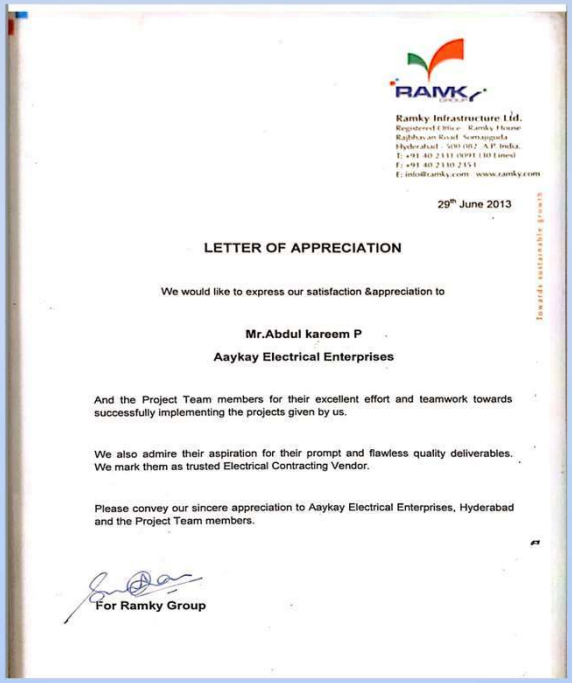

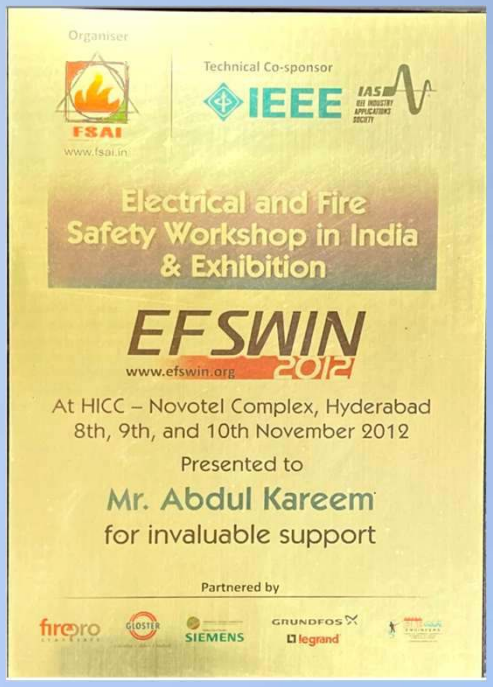


AWARDS & CERTIFICATIONS:







PROJECT MANAGEMENT AND GOVERNANCE:

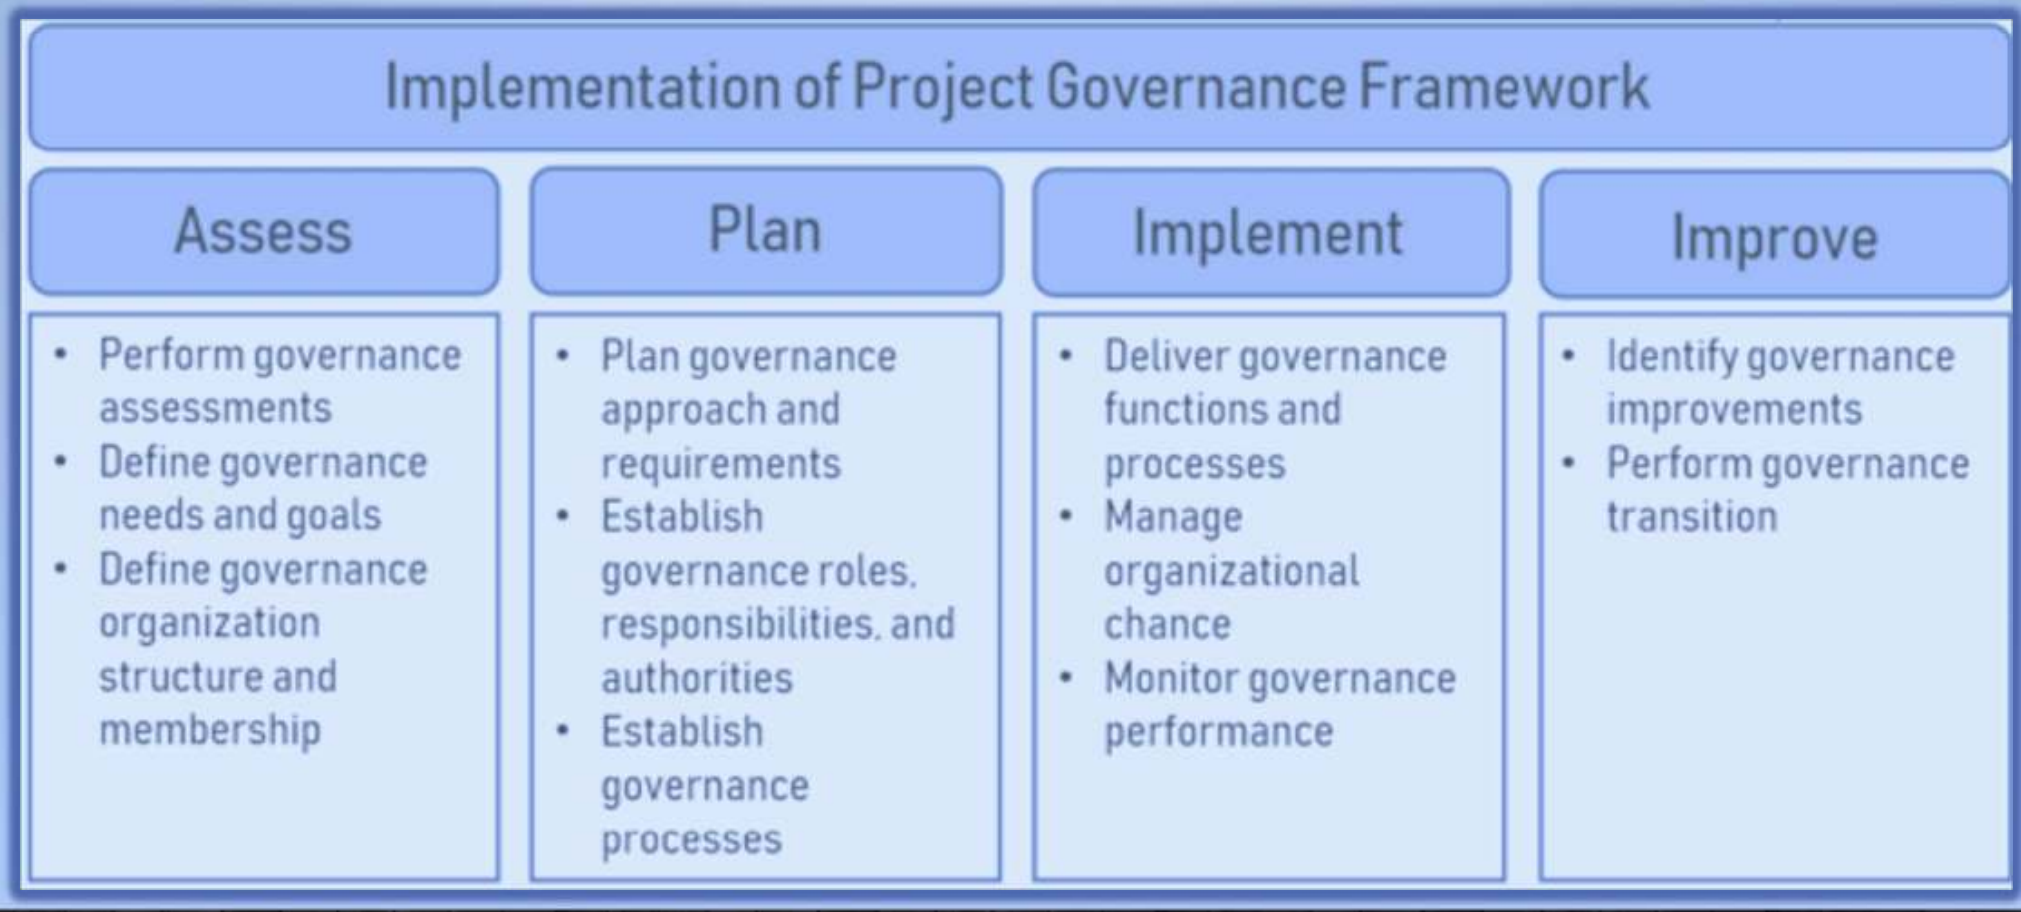

KEY INNOVATIONS:

- Uses of Battery-operated Dust free drilling & cutting machines with dust collector.
- Laser Tools usage for markings.
- Hydraulic machines for cable pulling in cable trays.
- Battery Operated tools.
- Factory fabricated items likes Cable trays Bends, T, L bend to overcome the fabrication time.


TESTING & COMMISSIONING



WE HAVE IN HOUSE TEAM FOR TESTING & COMMISSIONING FOR THE SYSTEM.



THE TEAM HAD TO COMPLETE RANGE OF TESTING EQUIPMENT TO PERFORM TESTING & COMMISSIONING INCLUDING INTEGRATED SYSTEM TEST AT THE SITE.



ALL SYSTEMS ARE TO BE TESTED AND COMMISSIONED AND SIGNED OFF BY PMC/CLIENT.

Testing Equipment's

Multimeter	Insulation	Multi-functional Tester	Digital Light Meter
			
Loop Impedance	RCD Tester	Torque Wrench	Thermal Imager
			
Infrared Thermometer	Phase Sequence meter	Digital Clamp on Meter	Earth Tester
			

DESIGN SYSTEM SOFTWARE'S:

AutoDesk REVIT BIM Software used for 3D & 2D designs, modeling and drafting with coordination of all MEP services

AutoDesk ACAD Software used for 2D designs, modeling, drafting and quantity take off as per requirements



COMPETENCE & STRENGTHS:

- We have Good tie ups & partnership with OEM team from past 15years.
- OEM Channels – LT panels (Schneider/L&T/ABB/Legrand), BusDucts & Raising Mains (Schneider/L&T/Legrand/EAE/C&S), LMS (Lutron/Crestron/Enlighten),
  Light Fixtures (Philips/Wipro/LT/ALW/XAL)
- And we are in good tie up more than one decade with our regular Manufacturers for LT panels & Cable trays for smooth delivery of materials

COMPANY RESOURCES:

RESOURCES	NOS (TOTAL)
MANAGEMENT & SUPERVISION	
PROJECT MANAGERS	15 NOS.
PROJECT ENGINEERS	30 NOS.
SUPERVISORS	60 NOS.
QUALITY STAFF	10 NOS.
SAFETY STAFF	15 NOS.
OFFICE STAFF	30 NOS.
WORK FORCE	
SKILLED LABOURS	500 NOS.
UN-SKILLED LABOURS	300 NOS.
SKILLED LABOURS-OUTSOURCED	200 NO.S
UN-SKILLED LABOURS-OUT SOURCED	100 NOS.

BEST PRACTICES THAT HAS BEEN IMPLEMENTED IN LAST 2YEARS AS VALUE ADD TO THE PROJECT:

S.No.	Description for value addition	Impact
1	Use of factory fabricated Raceway / Cable Tray supporting arrangement, clamps gripple support etc. as required	Time saving & best in quality
2	We have in house Testing & Commissioning Team	Time saving
3	Good Relation and Smooth Co-ordination with other agencies for delivery & service support.	No Delay in delivery & service support if required.
4	We have in house quality control team, complete safety & EHS Team, Planning & design facility.	Time saving on account of minor changes in drawings.
5	We have trained store and logistic team for checking of equipment & material as per boq	Time saving
6	Use of factory fabricated 25mm/32mm D clamp for installation of conduit & busbar trunking system.	Safety from water leakage & rusting from direct contact with floors.
7	Use of same color powder coated Raceway & Cable Tray as per Interior Finishes.	Best in quality
8	Use of Latest Testing Equipments, Tools & Tackles as per site requirement.	Time Saving
9	AayKay will deploy QA/QS team for quality check & balance to ensure to achieve the quality at first time.	Time saving & best in quality
10	AayKay will deploy dedicated Safety Manager for control in the safety as we have zero tolerance for safety.	Time saving & best in quality

SAFETY PLAN:

- The management of Aaykay Electricals Private Limited is committed to consistently Support Safety, Health and Environment systems.
- Towards this end, Aaykay Electricals Private Limited will ensure that.
- All its activities are carried out in a manner that provides reasonably practical safe and healthy environment for its employees and customers.
- Employees are trained to execute their work in a safe and environmentally responsible manner.
- Safety, Health and Environment care is exercised in its design and construction services.
- Safety, Health and Environment performance is continually improved.
- Aaykay Electricals Private Limited will implement this policy in compliance with Safety, Health and Environmental standards and codes of practice of its customers and in accordance with applicable national law and regulations.



Plan
- Policy
- Planning
- Hazard identification and risk assessment

Do
- Implementation and operation


Check
- Performance assessment (active and reactive)

Act
- Review and continual improvement

SAFETY PROCEDURES



TOOL BOX MEETING

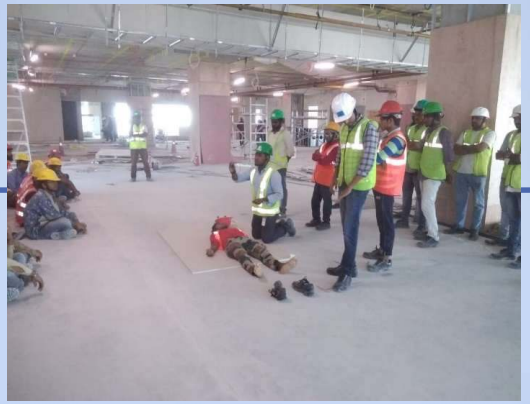

CPR TRAINING



TEMPORARY DB PRESENTAION



CABLE DRUM BARRICATION




WORK AREA BARRICATION DUIRING EXECUTION



CONDUITS BARRICATION



SAFETY MOCKUP

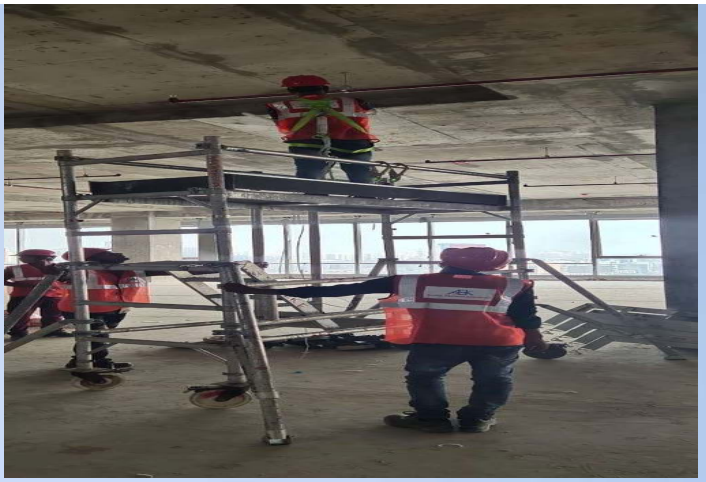

SCAFFOLDING WORKS UNDER SAFETY



TOOL BOX TALK



WORK AREA BARRICATION DUIRING EXECUTION






MEDICAL CHECKUP



SAFETY POSTERS

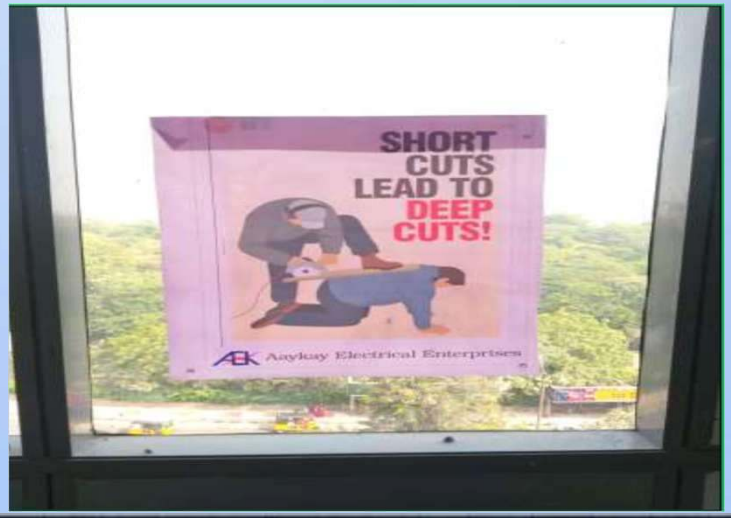

SAFETY AND SECURITY MEASURES REQUIREMENTS











The need to ensure the Safety and Security of the premise , man and material is most important. We need to ensure all safety measures to comply with the OHSE need.

At no given point of time the safety and security of the premise should get compromised. The OHSE document attached should be read in conjunction to the safety and security needs.

Key Elements

- Caution Tape
- Caution Cones
- Double Layer Safety Net
- Caution Signage: No Entry
- Caution Signage: Area Under Construction
- Caution Signage: Hard Hat Area
- Caution Signage: Workers Enter Here
- Caution Signage: Danger
- Caution Signage: Mind Your Head

Safety System in place at organisation level

- ERT team would be working 24/7 support services during any emergency
- Our safety team monitor each project closely and will be conducting virtual meeting on every alternate day to ensure safety standards are not compromised
- Weekly progress report on safety aspect will be viewed by top management and would be discussed at site safety team about this approach or any challenges been faced at site level
- Local hospitals tie-up will be monitored from organization level closely during any emergency time

AAYKAY ELECTRICALS PVT. LTD.

SAFETY POLICY

The Health, Safety and Environmental (HSE) policy enunciates the philosophy and commitment of the company towards environmental protection and management of health and safety of employees, contract workmen and visitors. The enhanced HSE policy is as follows

AayKay Electricals Pvt. Ltd. is committed to demonstrating a high standard of environmental protection, sharing of best practices and provision of a safe and healthy workplace.

To achieve this, we shall work towards :

Identification of HSE risks and opportunities in our operations

Environmental protection :

- We shall ensure sustainable resource usage.
- Ensuring all personal have clearly defined and understood responsibilities and accountabilities for the effective implementation of our HSE policy and management system.
- We shall work towards meeting our entire electricity demands from renewable energy through onsite or off-site sources.
- Engaging with contractor and other business partners to achieve and improve HSE standards.
- We shall explore and implement measures to mitigate impact of our operations on climate change.
- We shall work towards pollution prevention.
- Eliminating unsafe incidents, prevention of occupational illness and injuries at the workplace:

AAYKAY ELECTRICALS PRIVATE LIMITED

INTEGRATED MANAGEMENT SYSTEM (IMS) POLICY

AAYKAY ELECTRICALS PRIVATE LIMITED is committed to delivering safe, reliable, and high-quality electrical engineering services by integrating the principles of ISO 9001:2015 (Quality Management System) and ISO 45001:2018 (Occupational Health & Safety Management System) into all aspects of our operations.

We are committed to:

- Delivering electrical services that consistently meet or exceed customer expectations, with a focus on quality, reliability, and timely execution.
- Placing customer satisfaction at the core of our operations by understanding, anticipating, and fulfilling client requirements with accountability and professionalism.
- Preventing work-related injuries and ill health by identifying, eliminating, and controlling occupational health & safety risks at all levels of our activities.
- Complying with applicable legal, regulatory, and other requirements related to quality, health, and safety.
- Promoting a culture of safety and continuous improvement by conducting structured training, ensuring competency, and reinforcing safe work practices.
- Ensuring participation, involvement, and consultation of workers in quality and OH&S-related decision-making processes.
- Establishing and reviewing measurable IMS objectives to drive continual improvement through internal audits, incident investigations, corrective actions, and management reviews.

This policy is communicated to all employees and persons working on behalf of the company. It is displayed prominently at all work locations and made available to interested parties upon request. The policy shall be periodically reviewed to ensure its continued suitability, adequacy, and effectiveness.

Managing Director

Doc No: AKEPL/IMS/P/01 Rev-00, Effective date: 25-04-2025

- We shall identify hazards and assess risks pertaining to our operations on a periodic basis.
- We shall establish safety committees at all locations to monitor and control employee health and safety matters.
- We shall work on continually improving the maturity of our Emergency response practices for mitigating operational threats and vulnerabilities.
- We shall facilitate necessary Medical assistance to all personnel working in our organization as deemed appropriate and in line with policy guidelines.
- Determination of compliance obligations, adherence in all operations, monitoring to ensure fulfillment and correction of non-conformities.
- Embedding HSE culture in the organization.
- We will work with all interested parties to continually improve our Health, Safety and Environmental Management System.
- We shall meet mandated health and safety requirements as a minimum and strive to go beyond regulatory limitations to become an innovative leader in, health and safety and environment management as well to establish.

Our work is never so urgent or important that we cannot take time to be complaint with our values and do it in a safe, Health and Environmentally conscious manner.

Abdul Kareem
Managing Director.

"This is computer generated document no signature required."

SITE CHALLENGE, KEY PROJECT ISSUES & RISK ASSESSMENT:

S. No.	Description Of Risk	Impact	Mitigation Plan
1	GA Drawing approval & delivery of LT Panels	Delay in Manufacturing of equipment	Order Placement, submission & approval should be closed within timeline
2	Delivery of Light Fixtures	Safety / Time line / Quality	Order Placement, submission & approval should be closed within timeline
3	Delivery of LMS	Safety / Time line / Quality	Order Placement, submission & approval should be closed within timeline
4	Delivery of Raising Mains & Busducts	Safety / Time line / Quality	Order Placement, submission & approval should be closed within timeline

Project Name : UPCOMING PROJECTS

Date:05-11-2025

Completed by : Syed qadeer

LIKELIHOOD (L)	
Almost Certain	Could happen anytime
Likely	Could happen sometime
Unlikely	Could happen, but very rarely
Very Unlikely	Could happen but probably never will

CONSEQUENCE (C)	
Catastrophic	Death or permanent disability or permanent illness.
Major	Long term injury or serious illness lasting more than 7 days.
Moderate	Medical attention and less than seven days off work.
Minor	First Aid needed.

	Likelihood (L)			
Consequence (C)	Almost Certain	Likely	Unlikely	Very Unlikely
Catastrophic	E	E	H	M
Major	E	H	M	L
Moderate	H	M	L	L
Minor	M	L	L	L

Risk Response Guide		
Risk Score		Risk Response
E	Extreme	Work not to proceed until further mitigation is implemented.
H	High	Requires national review and approval to perform this activity.
M	Medium	Requires location/sector review and approval to perform this activity.
L	Low	Can be performed using existing standard controls and plans.

Date	Revision No.	Details of the Revision	Section	Page(s)

Project HS Risk Assessment (HIRA)

Marking at height	# Fall hazard to workers # Fall of materials and hitting to underneath personals	H	Ensure the work Platform is stable by inspecting the following points. a) Is the ladder complying with itschecklist a) Is the height of the ladder issufficient. a) Is the ladder placed on hard and even surface # Wear safety belt and hookup with rigidsupport.	L
Making holes on RCC moulds and Brick walls by using hammering machine	#Electrocution Twisting of hand due to over load on drillbit Fire hazard # Injury to eyes # Failure of abrasive wheel and resulting into multiple injury's. Fall of materials and hitting to underneath personals	H	# Use proper ladders to access the heights. # Don't keep any loose materials at the edge of working plat forms. # Use guide rope to lift or lower the materials. # Ensure height work permit # Ensure that Hammering machine was double insulated or Earthed properly. # Inspect for incoming Power supply conductor was properly insulated. # Draw the power from ELCB operated power socket. # Lay the temporary cables away from sharp edges and walk ways. # Be cautious to manage the jam of drill bit while hammering. # Don't over load the hammering machine # Don't lock the trigger butter of hammering machine	L

Project HS Risk Assessment (HIRA)

Major Work Activity	Potential Hazards	Risk Score	Possible Controls	Controlled Risk Score
Grinding / wall cutting	Fire hazard # Injury to eyes # Failure of abrasive wheel and resulting into multiple injury's. Fall of materials and hitting to underneath personals	H M	Clear the combustible materials from hot work area. # Keep fire extinguisher near the hot work # Wear safety goggles /visor. # Check mounting and tightness of abrasive wheel. # Adjust the guard asrequire. # Don't over load the abrasive wheel. # Don't sit exactly in front of cutoff machine Be aware of sharp edges and wear hand gloves. # Use guide rope to lift or lower the materials # Don't stop any job at half of the way. # Secure and tie the objects at end of the day # Barricade the work location. ## Use guide rope to lift or lower the materials	L L
Laying of conduits, Cable trays and race ways				

Project HS Risk Assessment (HIRA)

Major Work Activity	Potential Hazards	Risk Score	Possible Controls	Controlled Risk Score
Selection of A type ladder	# Tilting of Ladder	M	# Restrict the A type ladder height to max ten feet. # Don't stand on the top of the ladder	L
Inspection of ladder	Improper installation of rivets, Bolt and nuts may result into collapse	M	# Inspect all the revetments of ladder # Inspect all the bolt and nuts. # Ensure all the base of transoms are equal.	L L
Usage of A type ladder	Tilting of ladder	M	# Lock the doors and windows while using A type ladders near to doors and windows. # Deploy one person to hold the Ladder # Don't allow any person to work from platform of the ladder. # Stand on the third rung from top and perform the job. #worker should not stand on the ladder in opposite position. # Don't perform any heavy jobs by using A type ladder.	

Project HS Risk Assessment (HIRA)

Major Work Activity	Potential Hazards	Risk Score	Possible Controls	Controlled Risk Score
Straightening of GI & Cu strip	# Injury to personal by hitting of strip	H	# Deploy competent persons to hold the GI strip, while straightening to avoid unexpected bounce. # Do barricade the work area to avoid un wanted entry of personals	M
		H	# Don't perform this job near to the other equipment's, Electrical DBs etc.	M
Shifting of GI& Cu strip to work location and Laying of GI & Cu strip	Hitting to other personals		# Don't shift the lengthy strips by deploying single person. # Mind the over head electrical cables while shifting GI strips.	
		H	# Mind the movement of other personals near tunings and stair cases. Fallow the Precautions mentioned in Approved Risk Assessment of Fabrication jobs.	

Project HS Risk Assessment (HIRA)

Welding	# Fire hazard # Electrocution.	H	# Clear the combustible material from hot work area. # Keep the fire extinguisher near hot work area. # Don't perform any painting work near hot works. # Don't perform any hot works near flammable chemicals like Diesel, thinner. # Use Proper rated conductor to draw the power to welding machine. # Ensure proper earthing and shock preventer # Ensure hot work permit # Use industrial type plug tops to draw the power.	M
	# Injury to eyes	H	# Draw the power from ELCB operated power socket # Ensure continuity of body earth. # Wear hand gloves # Ensure all the live conductors are properly insulated.	M
Grinding & Cutting	# Failure of abrasive wheel and resulting into multiple injury's.		# Follow the above said safety measures to minimize hazards. # Wear safety goggles # Check mounting and tightness of abrasive wheel. # Adjust the guard as require. # Don't over load the abrasive wheel. # Don't close the ON/ OFF trigger with insulation tape , GI wire etc. # Do the cutting operation from left side of machine # Don't sit exactly behind the cutoff machine. # Clouse the sliding type guard, while work in progress # Don't over load the abrasive wheel.	

Project HS Risk Assessment (HIRA)

Preparation of cement mortar	# Heath hazard # Air Pollution	M	# Wear Dust mask, while mixing the cement mortar # Don't mix the cement mortar at open place, where the wind flow is more. # Don't mix the cement on mother soil, Use GI sheet or Plastic sheet to mix the cement mortar	L
Cementing works to fixing of DBs, Modular boxes and plastering to Earth pits.	# Trip and Fall hazard # Falling of Objects on personals # Electrocution	H	# Provide the barricading to materials like brick and cement mortar. # Don't stop any fixing job at half of the way, Until the same is properly secured. # Don't allow any person to underneath the fixing works, Until the masonry work get dried. # Isolate the nearby power supply, while curing the cementing jobs.	L
Storage of Paints and Thinner	# Fire Hazard # Health Hazard	M	# Lid of the container should be closed properly # All the paints and Thinners must be stored separately & away from power sockets and cable joints. # Keep the stand by fire extinguisher # Follow the instructions of MSDS # Wear mask to minimize the inhalation	L
Painting to MS structures	# Fire Hazard # Soil Contamination &Air Pollution Health Hazard	H	# Maintain at least five meters distance away from hot works, while doing the manual painting. # Maintain at least Ten meters distance away from hot works, While doing the Spray Painting # Consider the wind direction, While doing spray paint at outdoor. # Place the HDPE Sheet at underneath the painting job to avoid spillages on mother soil. # Don't carry the spray painting job at outdoor during the heavy winds. # Conduct the Tool box talk and Explain the objects and recommendations as per MSDS before start the painting job. # Don't use thinner as a cleaning agent	L L

Project HS Risk Assessment (HIRA)

Drilling for support of Cable Saddle installation,, Light Fixture installation, Cable tray clamping and raceway installation.	# Fire Hazard # Soil Contamination &Air Pollution Health Hazard	H	Use of PPE's like nose mask and Safety goggles is a must for this activity along with the mandatory PPE's Hammer drill used for this activity should be inspected and tagged SAFE TO USE by an electrician. Hammer drill should be routed through a 30mA ELCB. Workers should not stand on hand rails and work. Worker should work within the railings and toe guard.	L
Connection of wires and cables to electric Panel and DB dressing. Testing and commissioning	Electric Shock. Dust inhalation. Injury to eye. Fall from Height. Physical Injury. Ergonomic hazard. Electrocution. Fire. Burn Injury. Fatality.	M	Permit to Work' to be attained before commencement of work. Should ensure that the main incomer should not be connected to the panel. Licensed Electrician and skilled workers should execute the task to avoid incorrect connections. All cables dressed in the panel should be checked by a licensed electrician. Waste generated from DB dressing should be collected periodically and removed from the critical rooms. 100% Supervision needed for this activity. While applying 'Lock Out Tag out', electrical resistant Hand gloves to be used. 'Lock Out Tag Out' to be applied on the main panel while connecting it to the newly installed Electric Panels and DBs. Floor to be evacuated before removing the Lock Out Tag Out and switching on the supply. Fire extinguisher to be kept handy at all times.	L

Project HS Risk Assessment (HIRA)

Major Work Activity	Potential Hazards	Risk Score	Possible Controls	Controlled Risk Score

ThisHSRiskAssessmentconsidersonlythosepotentialhazardsthatexistatthetimeitwasconducted.ArevisedRiskAssessment willberequiredifthereisasignificantchangeinworkingconditions,atcriticalstagesduringconstruction,orwhenHighRiskConstruction Work is performed.

Signed:…… Print Name:…… Date:……

LABOUR WELFARE STRATEGY AND INITIATIVES:

We provide following facilities to our labours :

- Safety/PPE Equipment's (Safety Harness, Jackets, Helmets, Belt, & Shoes).
- Drinking water & Mobile Toilets.
- Snacks & Refreshment.
- Shifts allowance.
- Medical facilities provided.
- Temperature gun is provided to take the temperature of staff and labour before entering the site every day. Monthly medical camp is arranged to check the labour for fitness.
- Social Insurance Measures (including gratuity, pension, provident fund and ESI).
- Labour Toolbox Meeting.
- Manpower is trained to get aware about Coronavirus, ways it spreads, symptoms and precautionary measures to be taken.


LABOUR WELFARE STRATEGY AND INITIATIVES:

We maintain all the statutory documents required as per labor laws at site.

A dedicated person is assigned at site to ensure compliance to all the labor compliance documents applicable to us such as :

- Labor License
- ESI & PF documents
- Form 09: Register of workmen employed by the contractor
- Form 10: Employment card
- Form 11: Service certificate
- Form 12: Muster roll
- Form 13: Register of wages
- Form 15: Wage slip
- Form 16: Register of deductions for damages or loss
- Form 17: Register of fines
- Form 18: Register of advances
- Form 19: Register of overtime
- Leave register
- In-out register


LABOUR MANAGEMENT SYSTEM:

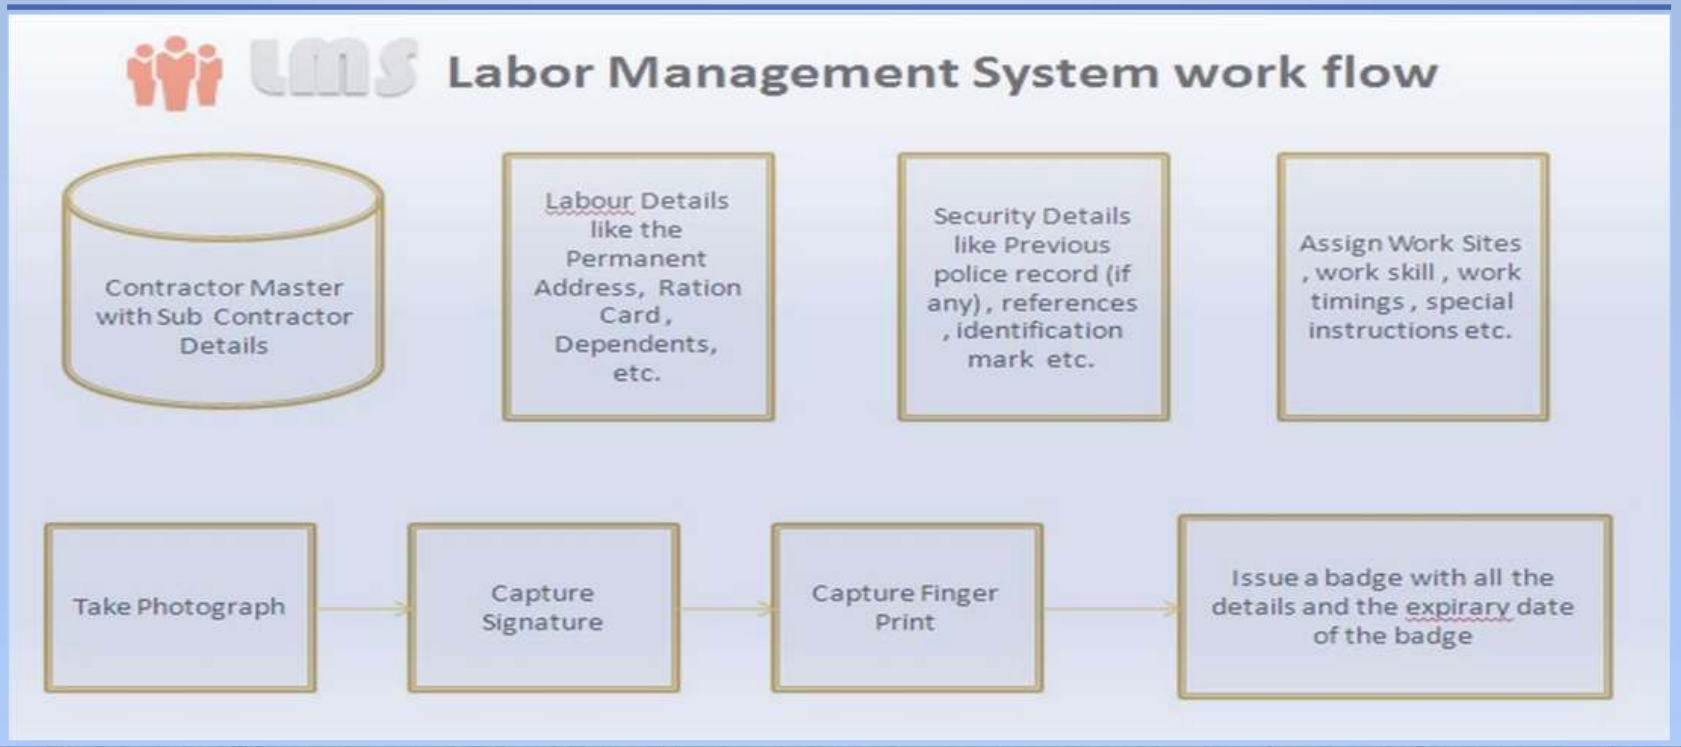

WASTE MANAGEMENT PLAN:

Microsoft Word Document

WASTE MANAGEMENT PLAN

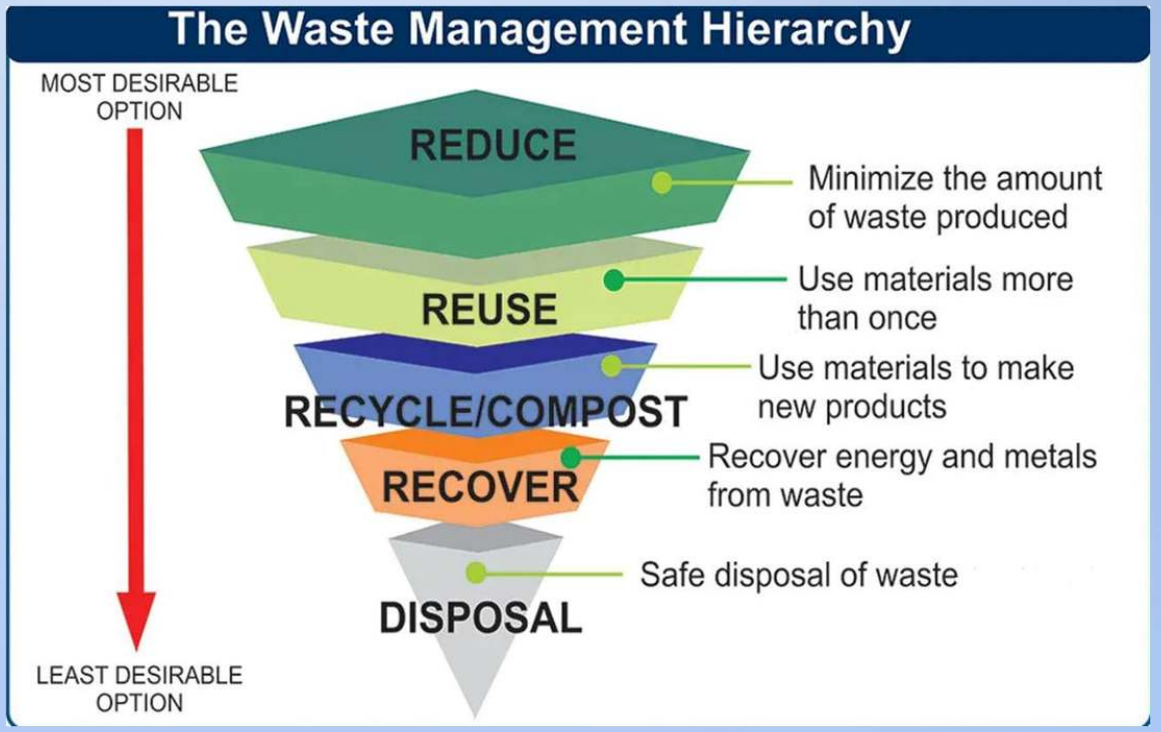

SIMILAR PROJECTS EXECUTED IN PAST:

HDFC Bank - Hyderabad

Scope of Works :	Internal Electrification Works
Project In Area :	100,000 SFT
No of Floors :	6 Floors
Work Order value :	3Cr
Architect :	Zyeta Architect
Electrical Consultant :	Hyderabad Consultant Engineers



Amazon MAA12 - Chennai

Scope of Works :	Internal Electrification Works
Project In Area :	475,000 SFT
No of Floors :	15 Floors
Work Order value :	10Cr
Architect :	M Moser Associates
Electrical Consultant :	Eshwari & Co



HDFC Bank - Hyderabad

Scope of Works :	Internal Electrification Works
Project In Area :	150,000 SFT
No of Floors :	4 Floors
Work Order value :	1Cr
Architect :	NA
Electrical Consultant :	Hyderabad Consultant Engineers



Cognizant Technologies - Coimbatore

Scope of Works :	Internal Electrification Works
Project In Area :	220,000 SFT
No of Floors :	4 Floors
Work Order value :	7Cr
Architect :	Venkataramanan Associates
Electrical Consultant :	Lead Consulants




Legato - Hyderabad

Scope of Works :	Internal Electrification Works
Project In Area :	300,000 SFT
No of Floors :	3 Floors
Work Order value :	4Cr
Architect :	Space Matrix Design & Consultants
Electrical Consultant :	Space Matrix Design & Consultants



Service Now - Hyderabad

Scope of Works :	Internal Electrification Works
Project In Area :	200,000 SFT
No of Floors :	4 Floors
Work Order value :	3Cr
Architect :	Space Matrix Design & Consultants
Electrical Consultant :	Space Matrix Design & Consultants

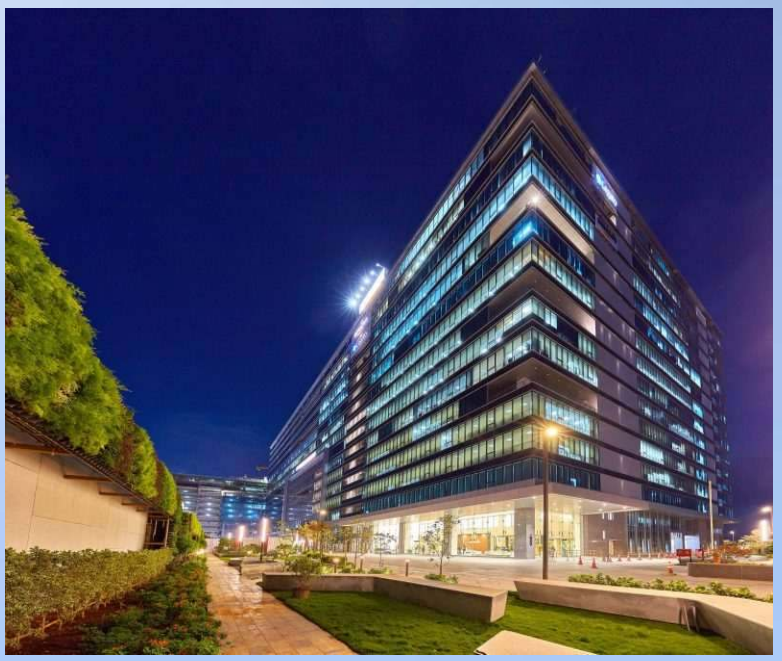

Accenture BDC 14 - Bengaluru

Scope of Works :	Internal Electrification Works
Project In Area :	200,000 SFT
No of Floors :	4 Floors
Work Order value :	3.5 Cr
Architect :	RSP Design Consultant India Pvt Ltd
Electrical Consultant :	RSP Design Consultant India Pvt Ltd



Walmart- Bengaluru

Scope of Works :	Internal Electrification Works
Project In Area :	250,000 SFT
No of Floors :	5 Floors
Work Order value :	6.5 Cr
Architect :	DSP Design Associates Pvt Ltd
Electrical Consultant :	Lead Consultant



Sequoia Capital- Bengaluru

Scope of Works :	Internal Electrification Works
Project In Area :	50,000 SFT
No of Floors :	6 Floors
Work Order value :	2.5 Cr
Architect :	Space Matrix Design & Consultants
Electrical Consultant :	Space Matrix Design & Consultants



Shell @ Bagmane Xenon -Bengaluru

Scope of Works :	Internal Electrification Works
Project In Area :	2,70,000 SFT
No of Floors :	5 Floors
Work Order value :	8 Cr
Architect :	Raj Consultant Pvt Ltd
Electrical Consultant :	Techtron Engineering Consultancy



- **MY HOME GRAWA-KOKAPET**

G+49 (1 TOWER)

1274000 SQFT

KOKAPET

MY HOME CONSTRUCTION

ON GOGING PROJECT



- **VASAVI ANANDA NILAYAM**

G+30 (I TOWER)

936000 SQFT

LB NAGAR

VASAVI GROUPS

ON GOGING PROJECT



- **MY HOME NISHADA**

G+44 (2 TOWER)

1800000 SQFT

KOKAPET

MY HOME CONSTRUCTION

ON GOGING



- **RAMKY ONE HARMONY**

G+9 (5 TOWER)

1178400 SQFT

PRAGATI NAGAR

RAMKY ESTATEES LTD

COMPLETED PROJECT-2025.



- **MY HOME TRIDASHA**

G+30 (2 TOWER)

3379200 SQFT

TELAPUR

MY HOME CONSTRUCTION

COMPLETED PROJECT-2024



KSH-Hospital - Hyd

Scope of Works :	Internal Electrification Works
Project In Area :	774,000 SFT
No of Floors :	24 Floors
Work Order value :	14 Cr
Architect :	ARKK CONSULTING
Electrical Consultant :	ARKK CONSULTING



KIMS Hospital (KONDAPUR) - Hyd

Scope of Works :	Internal Electrification Works
Project In Area :	130,000 SFT
No of Floors :	10 Floors
Work Order value :	1.75Cr
Architect :	SYNERGY
Electrical Consultant :	SYNERGY



YASHODA Hospital PROJECT-1 (Soajiguda)-Hyd

Scope of Works :	Internal Electrification Works
Project In Area :	150,000 SFT
No of Floors :	11 Floors
Work Order value :	2.11Cr
Architect :	SYNERGY
Electrical Consultant :	SYNERGY



YASHODA Hospital PROJECT-11 (Soajiguda)-Hyd

Scope of Works :	Internal Electrification Works
Project In Area :	396,000 SFT
No of Floors :	11 Floors
Work Order value :	4.7 Cr
Architect :	SYNERGY
Electrical Consultant :	SYNERGY



YASHODA Hospital PROJECT-III (Secunderabad)-Hyd

Scope of Works :	Internal Electrification Works
Project In Area :	120,000 SFT
No of Floors :	11 Floors
Work Order value :	1.78 Cr
Architect :	SYNERGY
Electrical Consultant :	SYNERGY



OUR REPEATED CLIENTS:



















SOME OF OUR CURRENT PRESTIGIOUS PROJECTS



Krishna Sindhura Hospital - Hyderabad



HDFC Bank - Hyderabad



Tech Mahindra – Hyderabad



Network 18 - Noida



Bosch - Coimbatore



NCR - HYDERABAD

Bagmane Cosmos Tech Park – External Electrification Works

- **ARIEL**
- **VESTA**
- **MLCP**
- **VESTA EXTENSION**



CLIENT LIST


amazon


IBM


HDFC BANK


AMD


cognizant


alliantgroup


infor


Microsoft


NCR


accenture


D E Shaw & Co


MY
HOME
GROUP



RAMK
GROUP
Towards sustainable growth


TECH
mahindra


Network 18


BOSCH
CtrlS
servicenow
SATTVA
TRUST, IT'S WHAT WE BUILD.
JLL
Uber
pwc
BERKADIA
virtusa
CBRE
Medtronic
Qualcomm
wework
CUSHMAN & WAKEFIELD
GMR
invisalign
Legato

WHY AAYKAY?

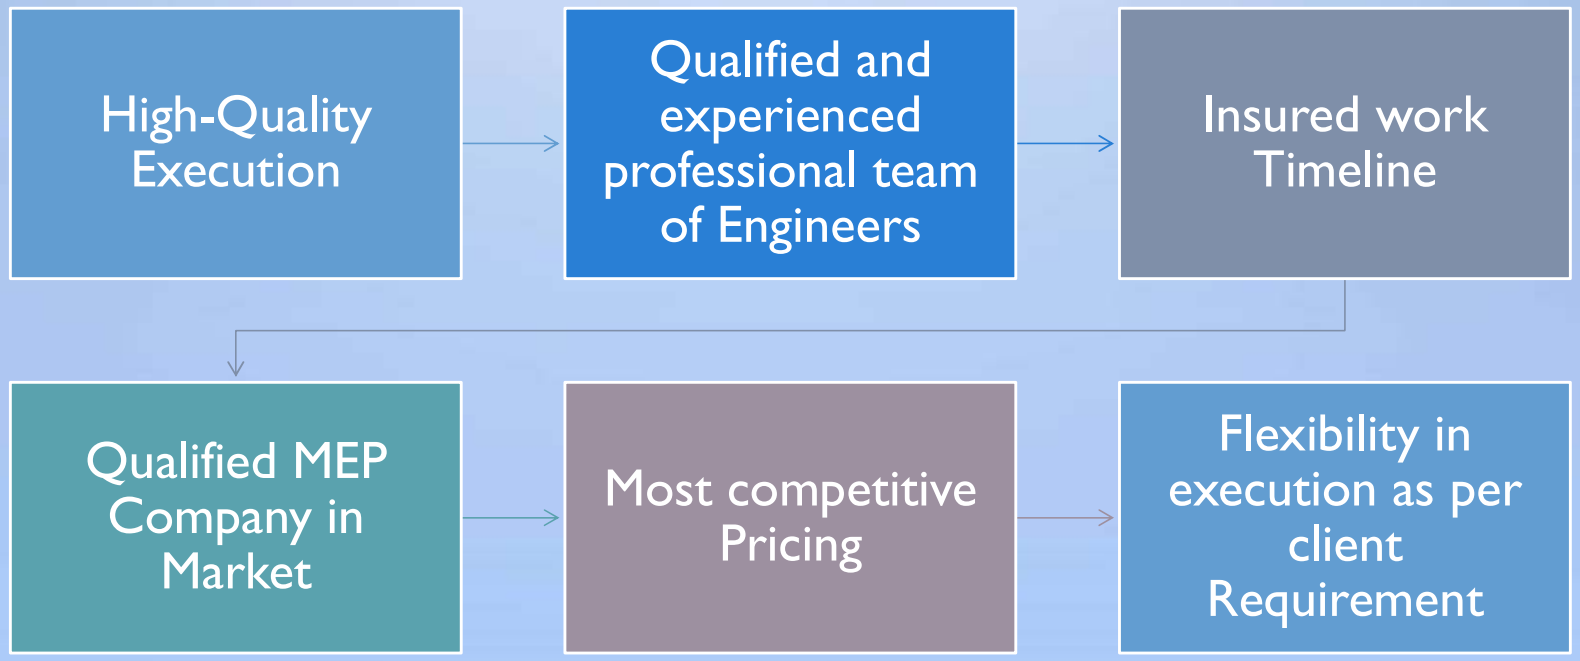
High-Quality Execution
Qualified and experienced professional team of Engineers
Insured work Timeline
Qualified MEP Company in Market
Most competitive Pricing
Flexibility in execution as per client Requirement


Q
&
A

Thank you!

Look forward for a long-term association!!
